


# Chemistry Building Renovation

Construction Update – Week of March 14<sup>th</sup>, 2022

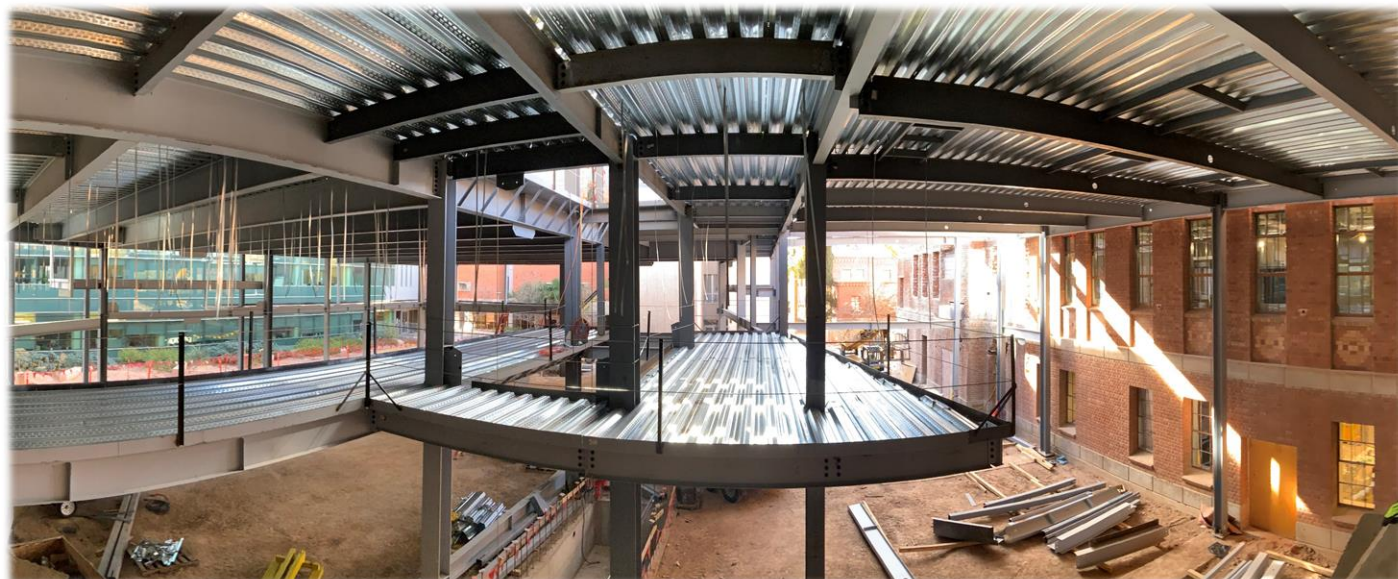

**The Commons Deck** is complete! Iron workers will finish up welding and installing mechanical screen supports on the roof.

Architectural Rendering



# Chemistry Building Renovation



Construction Update – Week of March 14<sup>th</sup>, 2022

**Openings:** Lots of new openings in the old brick will help make the space feel more open.



**Level 2:** Hallways have taped dry wall, cable tray and duct work installed overhead.

**Level 3:** Follows behind level 2 with framing and dry wall hung from above.



**Level 1:** Demolitions of the north hallway to make room for a new elevator

