



Chemistry Building Renovation

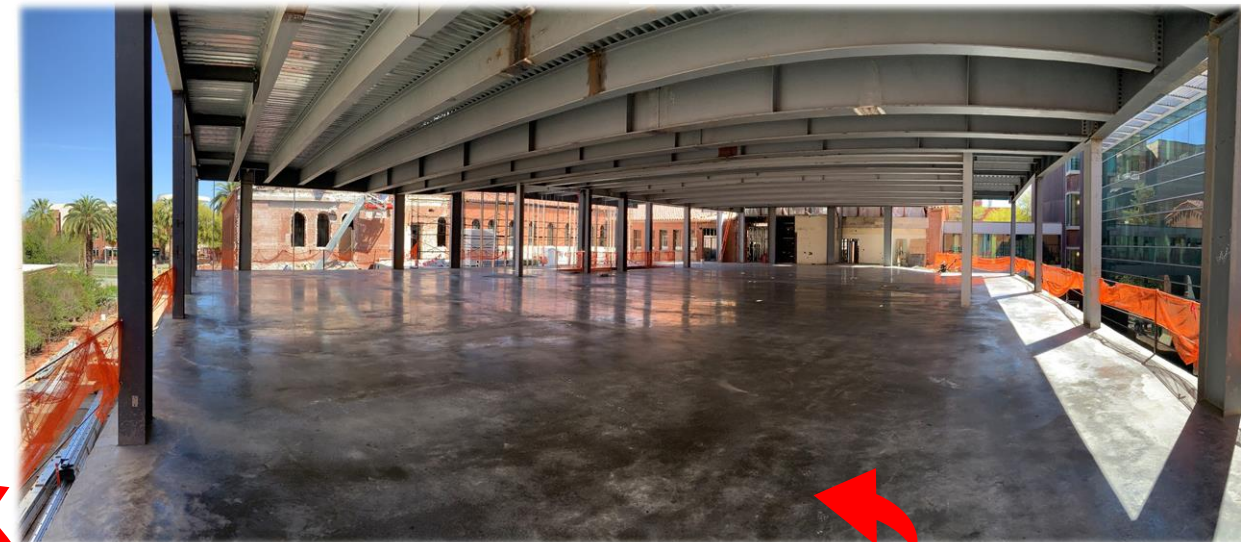


Construction Update – Week of April 11th, 2022

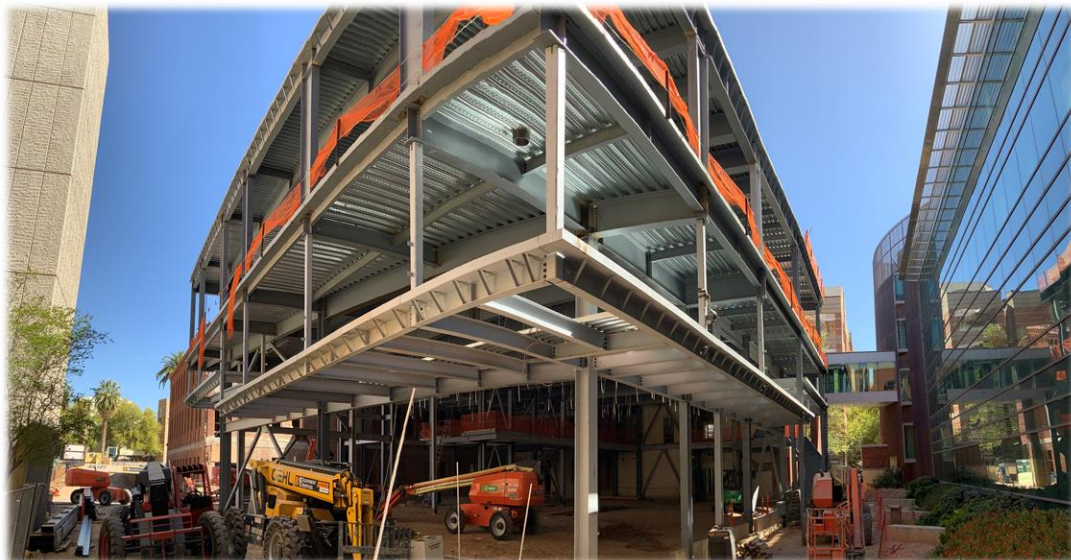

The Commons Level 2 and 3 have concrete. Mechanical and Electrical lay out will begin, and interior walls will be coming soon.

Level 3 Concrete is placed

Architectural Rendering

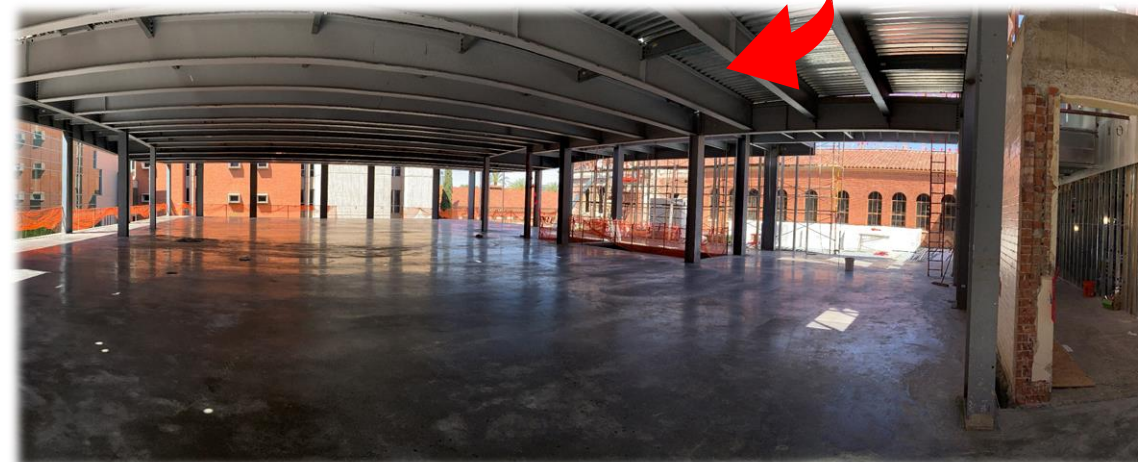

Chemistry Building Renovation


Construction Update – Week of April 11th, 2022

Exterior: Exterior framing has begun to close in the new building



Level 3: Insulation is being hung and duct work is going up through the roof of the existing building and will connect to the new building

Level 2: Saw cutting through the existing block wall to create a new entrance to the room

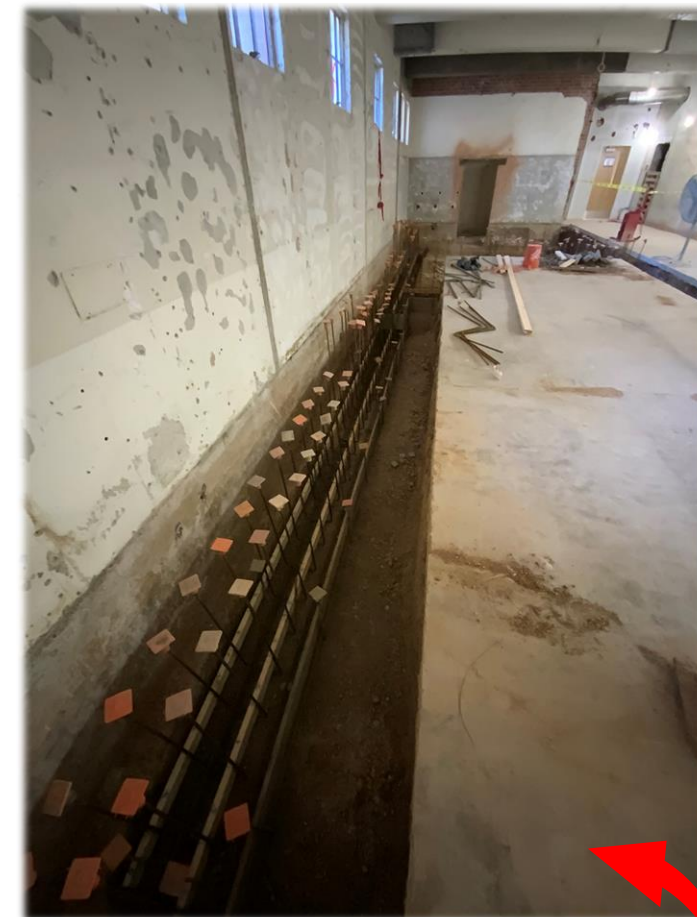

Level 1: This grade beam will support the piers required to remove the second floor and create an accessible entrance from the mall

